MOUNT NEBO ROAD REMEDIATION SEGMENT 2A

PROJECT UPDATE WEEK ENDING 3 August 2018

Project Overview

Moreton Bay Regional Council is undertaking road construction works to improve a 350m section of Mount Nebo Road. Once complete, the project will provide improved traffic flow with enhanced safety for road users.

The works are being carried out by Hazell Bros.

Works completed this week:


- Construction of Gabion Walls G2 and G3 continuing from Chainage 6880 to 6920.
- Installation of cross road drainage pipes
- Removal of vegetation and boulders from high side embankments
- Excavation for Gabion Wall G3 from Chainage 6920 continuing.
- Preparing roadbase level for low side lanes.

Works planned for week commencing Monday 6 August 2018

- Continuing Gabion Wall G2 and G3
- Installation of roadbase
- Installation of cross road drainage pipes
- Commence installation of Greenax embankment stabilisation.

NOTE: Traffic restrictions continue on this section of Mount Nebo Road.

- Road closure 8am to 4.30pm on 6th, 7th, 8th, 9th and 10th August
 - to allow installation of Greenax mesh to high side embankment and further drainage pipes
- Road closure 8am to 4.30pm 13th, 14th, 15th, 16th and 17th August
 - to allow installation of Greenax mesh to high side embankment, profiling of the existing high side road and installation of new roadbase layers.
- Traffic control diversion in place via Forestry Road

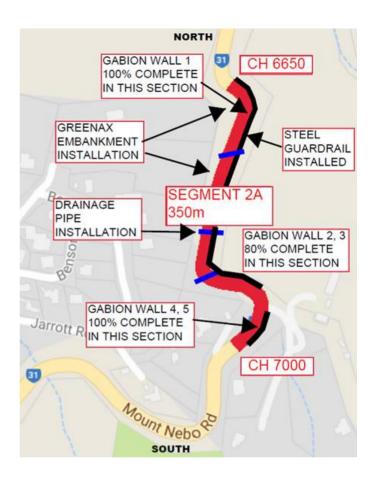

ROAD CLOSURE PHOTO MAP





Wall G2 looking south



Embankment to be stablisied with Greenax. Boulder removed from embankment. (looking south towards wall G2)
