

MOUNT NEBO ROAD REMEDIATION SEGMENT 2A

PROJECT UPDATE

WEEK ENDING 4 May 2018

Project Overview

Moreton Bay Regional Council is undertaking road construction works to improve a 350m section of Mount Nebo Road. Once complete, the project will provide improved traffic flow with enhanced safety for road users.

The works are being carried out by Hazell Bros.


Works completed this week:

- Construction of Gabion Walls G1 continuing from Chainage 6650 to 6750
- Excavation for Gabion Walls G1 from Chainage 6750 to 6800 commenced.
- Construction of Gabion Wall G6 continuing from Chainage 6970 to 7000 (approx. 80% complete)
- Project Update to Mt Nebo Community on Wednesday evening 2 May.

Works planned for week commencing Tuesday 8 May 2018

- Continuing Gabion Wall G1 to Chainage 6750
- Installation of Soil Nails and Bored Piers from Chainage 6765 to 6795. Commence excavation for continuation of Gabion Wall.
- Continuing Gabion Wall G6.
- Minor road repairs to the live traffic lane.
- No temporary road closures planned for this week.
- Progress with Greenaxe mesh and embankment stabilisation on high side of road, replacing segmental block walls.

NOTE: Traffic restrictions continue on

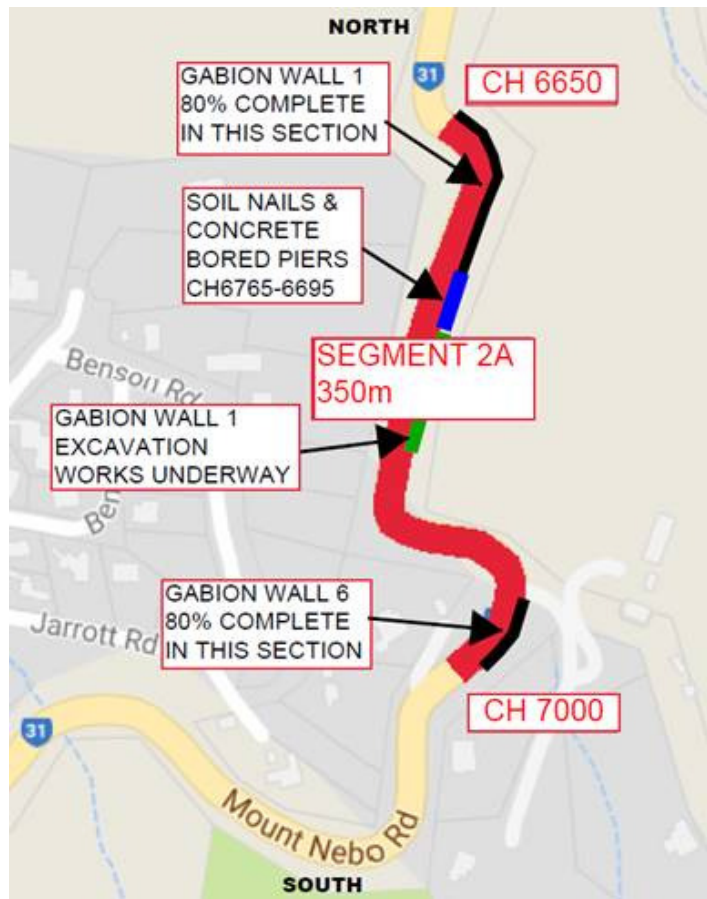

this section of Mount Nebo Road.



Progress with Wall G1



Progress with Wall G6
