

# MOUNT NEBO ROAD REMEDIATION SEGMENT 2A

## PROJECT UPDATE WEEK ENDING 8 June 2018

### Project Overview

Moreton Bay Regional Council is undertaking road construction works to improve a 350m section of Mount Nebo Road. Once complete, the project will provide improved traffic flow with enhanced safety for road users.

The works are being carried out by Hazell Bros.


### Works completed this week:

- Construction of Gabion Walls G1 continuing from Chainage 6650 to 6750
- Excavation for Gabion Walls G1 from Chainage 6750 to 6850 commenced.
- Excavation for Gabion Wall G2 from Chainage 6850 continuing. Soil nails placed in embankment. Concrete bored piers placed.
- Construction of Gabion Wall G6 continuing from Chainage 6970 to 7000 (approx. 100% complete)
- Road repairs to live lane carried out.

### Works planned for week commencing Monday 11 June 2018

- Continuing Gabion Wall G1 to Chainage 6850
- Soil nails continuing for Gabion Wall G2 from Chainage 6680.
- Temporary road closure planned for 14 June 2018.  
Notifications to be sent out Monday

**NOTE: Traffic restrictions continue on this section of Mount Nebo Road.**

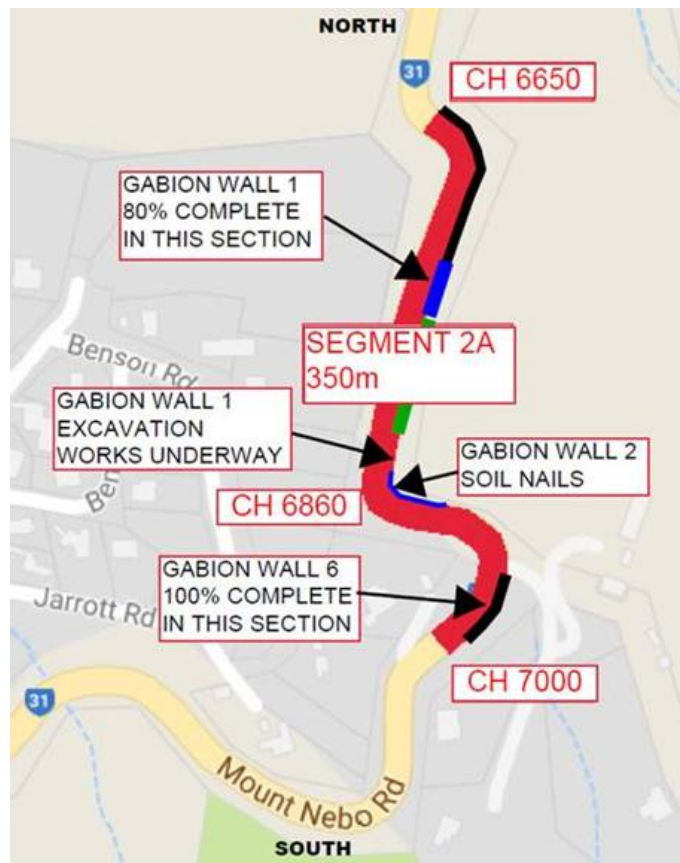

Excavation for Wall G2 commenced



Wall G1 continuing (looking north)
