

MOUNT NEBO ROAD REMEDIATION SEGMENT 2A

PROJECT UPDATE

WEEK ENDING 31 August 2018

Project Overview

Moreton Bay Regional Council is undertaking road construction works to improve a 350m section of Mount Nebo Road. Once complete, the project will provide improved traffic flow with enhanced safety for road users.

The works are being carried out by Hazell Bros.


NOTE: Traffic restrictions continue on this section of Mount Nebo Road until 9 September 2018. Road will then be opened for use.

Works completed this week:

- Construction of Gabion Walls completed.
- Asphaltic Concrete (AC) placed on Wednesday 29 August 2018 to whole of road section
- Installation of linemarking for road edge and centre
- Offset planting at Thomas Graham Court Park complete (2000 plants installed)
- Greenax Embankment Stabilisation on high side of road complete

Works planned for week commencing Monday 3 September 2018

- Installation of remaining guardrail from Chainage 6850
- Installation of roadside signage, RRPMS
- Installation of roadside rock drains
- Installation of 4 Variable Messages Signs - for posting of speed limit
- Road opening planned for Friday 7 September - weather dependant
- Commence embankment stabilisation on low side at Chainage 7000

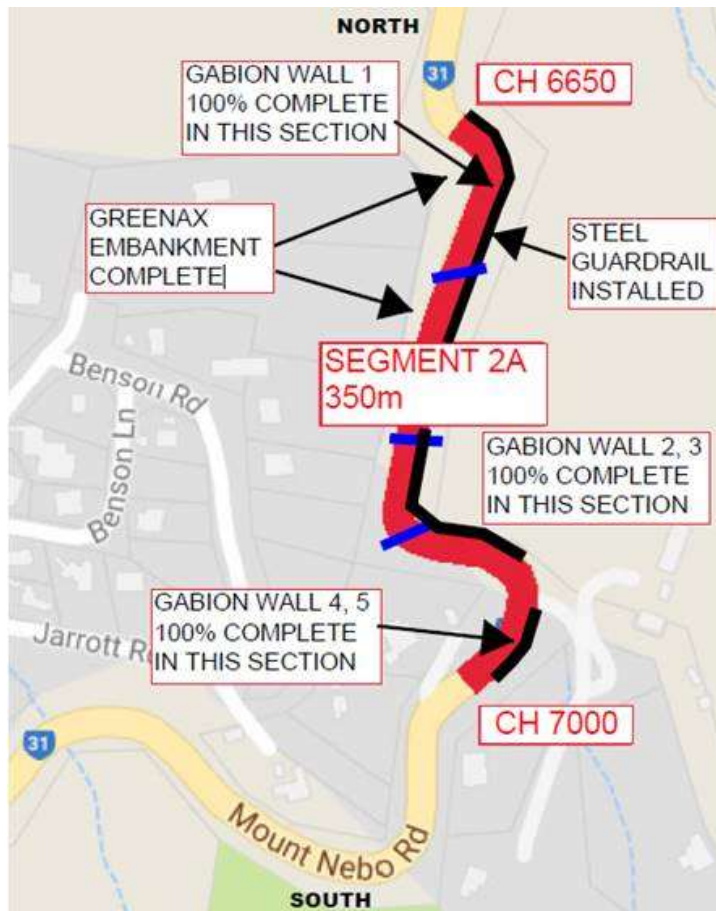

Laying of Asphaltic Concrete



Wall G2 looking south



Greenax embankment, Chainage 6900



Road at Chainage 7000 (looking north)
